

→ F T M



KEY ACTION STATUS

- ACTION PLAN FEB 1985
- ATTACHMENT MOA MARCH 1985
- HUMAN USE APPROVAL MARCH 1985
- SECURITY:
 - SPECIAL ACCESS PROGRAM MARCH 1985
 - COVER STORY APRIL 1985
 - PROCEDURES FOR PROTECTING VIEWERS IDENTITY MAY 1985
- TRANSFER TO DIA PENDING APPROVAL OF FY 86 AUTHORIZATION BILL

U2111.03



PERSONNEL SELECTION/CONTINUITY

- QUESTIONNAIRE
- FORMAL PROFILING
- TALENT POOL DEVELOPMENT
- PSYCHOLOGICAL REVIEW/
FOLLOW-UP
- STAFF CONTINUITY
- COMPLETE
- IN PROGRESS WITH RHR
- INITIATE BY FEB 1986
- MID 1986 (DIA, POSSIBLY INSCOM)
- PROCEDURES TO BE DEVELOPED
- ACTIONS CONSIDERED:
 - CONVERT SOME MILITARY SLOTS
TO CIVILIAN
 - ROTATE PREVIOUS MILITARY BACK
TO PROJECT

U2111.09




TRAINING

- SRI TRAINING METHODS IN USE
- BASIC TRAINING DURING FY85 PERFORMED IN-HOUSE
- TRAINING STATUS:
 - THREE IN STAGE 6
 - ONE IN MID-TRAINING
 - TWO WILL BEGIN OPERATIONAL TRAINING BY 1 FEB 86

S2111:12



TRAINING RESULTS (1985)

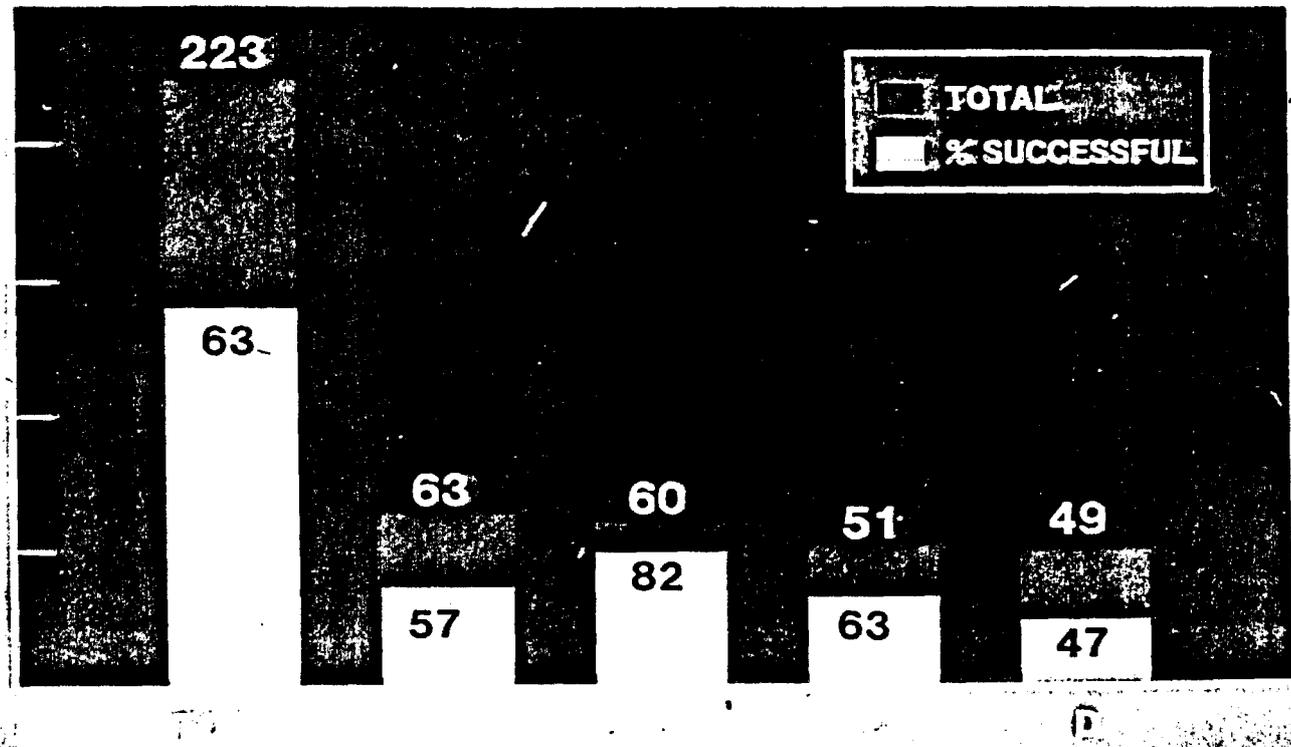

SECRET

S2111.23



DEVELOPMENT PHASE

PHASE

TIME REQUIRED

1. BASIC TRAINING

- 6 STAGES
- DRAWING/ART EXERCISES
- PERIODIC VALIDATIONS

- WAS TWO YEARS
- ANTICIPATE 1 YEAR FOR NEW PEOPLE
- NEW TRAINING METHODS MAY REDUCE TIME

2. OPERATIONAL TRAINING

- LIMITED OPERATIONAL STATUS
- OPERATIONAL STATUS
- PROJECT MIX (80% INTEL/SIMULATIONS
20% OPERATIONAL)

- 3 - 6 MONTHS
- 6 - 12 MONTHS

3. PERIODIC ADVANCED TRAINING

~~SECRET~~

S2111-10



OPERATIONAL ISSUES

- OPERATIONAL MANUAL COMPLETE; UPDATES AS REQUIRED
- OPERATIONAL TRAINING PACKAGE PARTIALLY COMPLETE; FINAL BY MID JAN 86
- OPERATIONAL STATUS CRITERIA COMPLETE
- PROCEDURES FOR PERFORMING OPERATIONAL TASKS
 - COMPLETE BY MID JAN 1986
 - IC TASK COORDINATING GROUP BY MID FEB 1986
- PROCEDURES FOR INTEGRATING DATA INTO INTELLIGENCE DATA BASE AND ASSESSMENTS TO BE DEVELOPED

S2111.16



SPECIFIC CRITERIA

- LIMITED OPERATIONAL STATUS
 - INDIVIDUAL
 - 50 PROJECTS
 - 60% SUCCESS
 - UNIT
 - MINIMUM OF TWO VIEWERS
 - QUALIFIED FOR 30% OF POTENTIAL TASKS

- OPERATIONAL STATUS
 - INDIVIDUAL
 - 100 ADDITIONAL PROJECTS
 - 80% SUCCESS ON THEIR STRENGTHS
 - UNIT
 - MINIMUM OF FOUR VIEWERS
 - QUALIFIED FOR 70% OF POTENTIAL TASKS

S21114



UNIT OPERATIONAL STATUS

- LIMITED READINESS EST MID 1987
 - TWO VIEWERS
 - SATISFACTORY RESULTS FROM FROM FIRST PART OF PHASE 2

- OPERATIONAL STATUS EST MID 1988
 - FOUR VIEWERS (2 TEAMS)
 - SATISFACTORY RESULTS FROM SECOND PART OF PHASE 2
 - DATA FROM PHASE 2 WILL PERMIT RELIABILITY ESTIMATES AND RESOURCE MIX SELECTION

S2111.13



DATA EVALUATION

- TRAINING PROJECTS
 - BINARY AND 0-3 LEVEL ACCURACY SCALE
 - ELEMENT ANALYSIS

- OPERATIONAL TRAINING
 - 0-3 LEVEL ACCURACY SCALE
 - CONCEPT ANALYSIS/ELEMENT ANALYSIS

- OPERATIONAL PROJECTS
 - 0-3 ACCURACY SCALE (CUSTOMER)
 - 0-3 OVER-ALL UTILITY (CUSTOMER)
 - POST HOC EVALUATION (PROGRAM MANAGER, IC TASK COORD GROUP)

S2111-15

SECRET NOFORN

UNIQUE FOR:


- INTERNAL FACILITY DATA
- NARROWING DOWN POSSIBILITIES
- CUEING OF OTHER ASSETS
- PREDICTIVE

SECRET NOFORN



SUN STREAK OPERATIONAL GROUP

SECRET

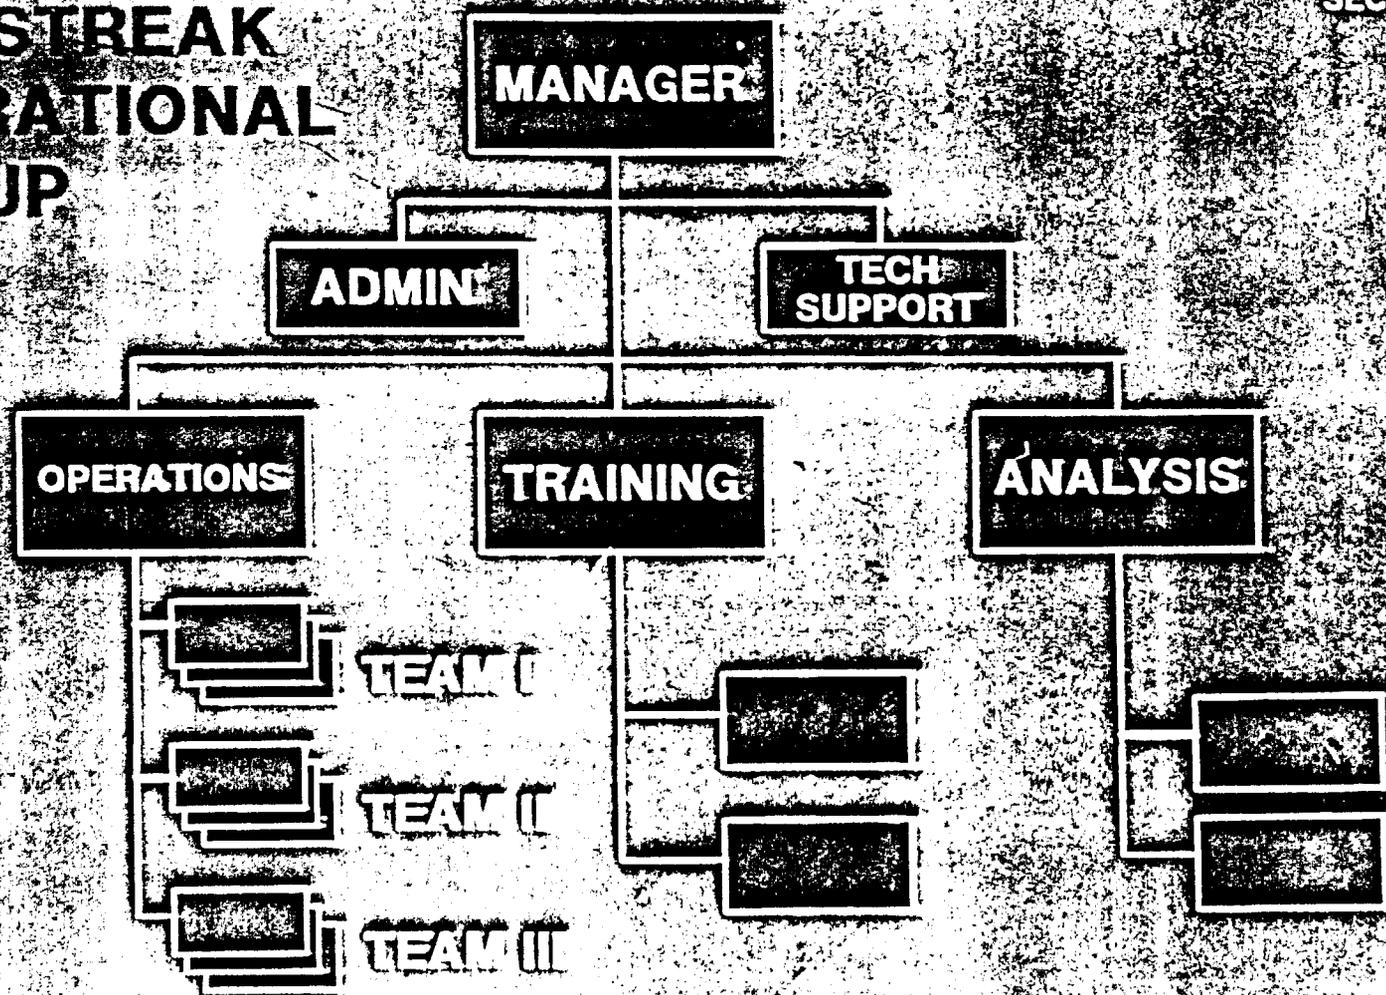

SECRET

SECRET

SECRET



EXTERNAL GDIP FUNDING NEEDS

<u>TASKS</u>	<u>FUNDING LEVEL (\$K)</u>	<u>TO BEGIN(FY)</u>
• ASSIST IN PSYCHOLOGICAL PROFILE DATA ASSESSMENT	50	87
• ASSIST IN TRAINING NEW IN-HOUSE PEOPLE	150	87
• SUPPORT OPERATIONAL PROJECTS	25	87
• IMPROVE SELECTION CRITERIA	100	87
• IMPROVE OPERATIONAL DATA EVALUATION METHODOLOGY	50	87
• DEVELOP NEW APPLICATIONS	100	88
• IMPROVE TRAINING EFFICIENCY	100	88

~~SECRET~~

S211117
